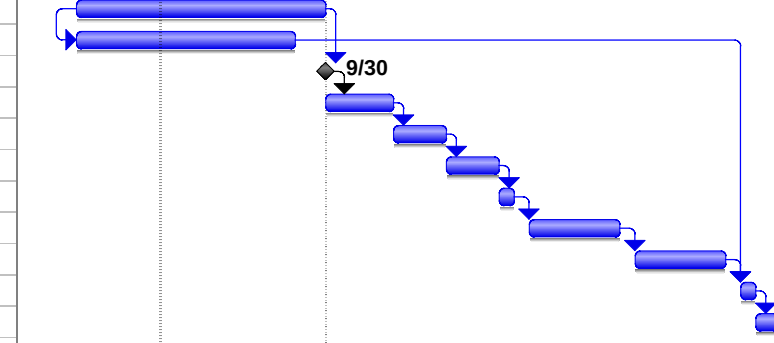


Minors A Proposed Schedule

August 29, 2019

ID		Task Name	Duration	Start	Finish	Predecessors	4th Quarter													
							E	B	M	E	B	M	E	B	M	E	B			
1		Complete Estimates	23 days	Thu 8/29/19	Mon 9/30/19															
2		Procure Bleachers & Backstop	21 days	Thu 8/29/19	Thu 9/26/19	1SS														
3		Start Construction	0 days	Mon 9/30/19	Mon 9/30/19	1														
4		Demolition	7 days	Tue 10/1/19	Wed 10/9/19	3														
5		Backstop Wall Footer	5 days	Thu 10/10/19	Wed 10/16/19	4														
6		Dugout Footers	5 days	Thu 10/17/19	Wed 10/23/19	5														
7		Backstop Wall	2 days	Thu 10/24/19	Fri 10/25/19	6														
8		Dugout Block	10 days	Mon 10/28/19	Fri 11/8/19	7														
9		Dugout Framing & Roofing	10 days	Mon 11/11/19	Fri 11/22/19	8														
10		Install Backstop Fencing	2 days	Mon 11/25/19	Tue 11/26/19	9,2														
11		Install Bleachers	3 days	Wed 11/27/19	Fri 11/29/19	10														
12		Project Complete	0 days	Fri 11/29/19	Fri 11/29/19	11														

Project: Proposed Schedule 8-29-2019
Date: Mon 9/9/19

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline

