

Pinon School Trail Connection Project &

NM4 Crossing & Multi-Use Trail Improvement Project Update

November 6, 2025





U.S. Department of Transportation

Federal Highway

Administration

INTRODUCTIONS



Keith Wilson

Deputy Public Works Director

Public Works Department

Phone: 505 663 1757

Email: keith.Wilson@losalamosnm.gov



John Stricklan P.E.

Project Manager

Public Works Engineering

Phone: 505 662 8117

Email: john.stricklan@losalamosnm.gov

Bohannan A Huston

Jared Lee Engineering Principal







PROJECT BACKGROUND

- February 2024 Pinon Elementary Trail Presentation Transportation Board
- December 2025 NM4 & Multi-Use Trail Presentation to Transportation Board
- January 2025 NM4 & Multi-Use Trail Presentation to Transportation Board
- January 2025 NM4 & Multi-Use Trail Presentation to Parks and Recreation Board
- March 2025 NM4 & Multi-Use Trail Presentation at County Open House
- June 2025 NM4 & Multi-Use Trail Presentation To Arts Council
- July 2025 NM4 & Multi-Use Trail & Pinon Elementary Trail Presentation to Sierra Vista Neighbors
- November 2025 NM4 & Multi-Use Trail & Pinon Elementary Trail Presentation to Transportation Board









Pinon School Trail:

• NMDOT CN5101970

Construction Funding

Federal Funds: \$598,080

<u>Local Match: \$101,920</u>

Total \$700,000

 Federal Funding = Transportation Alternative Program (TAP) Flex Funding FY26









PINON SCHOOL TRAIL CONNECTION PROJECT DETAILS

- Provides an ADA Compliant trail connection to Grand Canyon Drive and Pinon Elementary School from the NM-4 Crossing & Multi-Use Trail Project
- Full NEPA Procedures being followed.
- Easement has been obtained from Los Alamos Public Schools to allow this trail section to be incorporated into the project.
- ~850 linear feet of existing trail reconstruction along the west side of the school campus to improve the existing trail condition and accessibility.







PINON SCHOOL TRAIL Existing Conditions













PINON PARK

ADA Landings

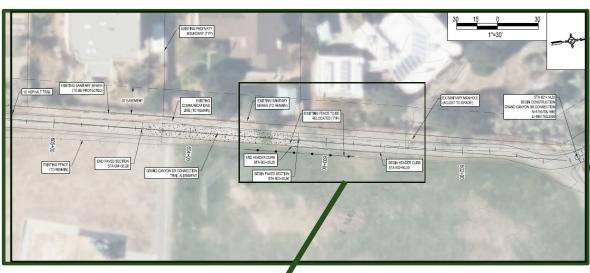



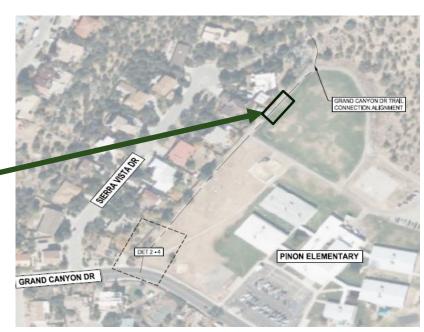



TRAIL TYPICAL SECTION

LEFT SLOPING - 10' TRAIL (1%) WITH BENCH & 3:1 TIE

NOT TO SCALE

GRAND CANYON DR CONNECTION 602+55,00 603+25,00








PINON PARK

Grand Canyon Drive Connection

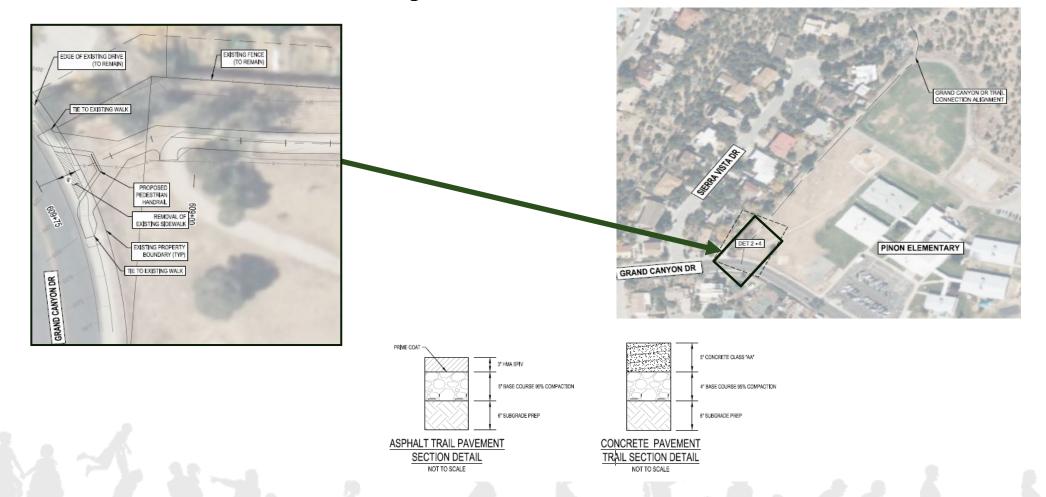









NM4 Crossing & Multi Use Trail:

NMDOT CN5101730

Design Funding

CMAQ CRP Federal Funds: \$213,600 Local Match: \$36,400 Total \$250,000

Construction Funding

 CMAQ CRP Federal Funds:
 \$2,136,000

 Local Match:
 \$364,000

 Total
 \$2,500,000

Design Complete August 2025











NM4 Cross Section Existing Conditions












NM4 Cross Section New Condition

Lane reduction, Concrete Barrier and and New Hawk Signal

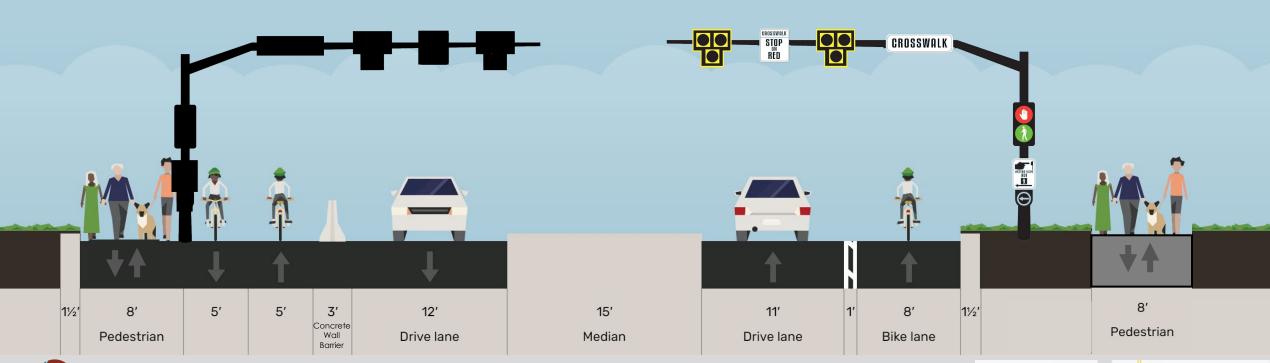








NM-4 Trail Plan

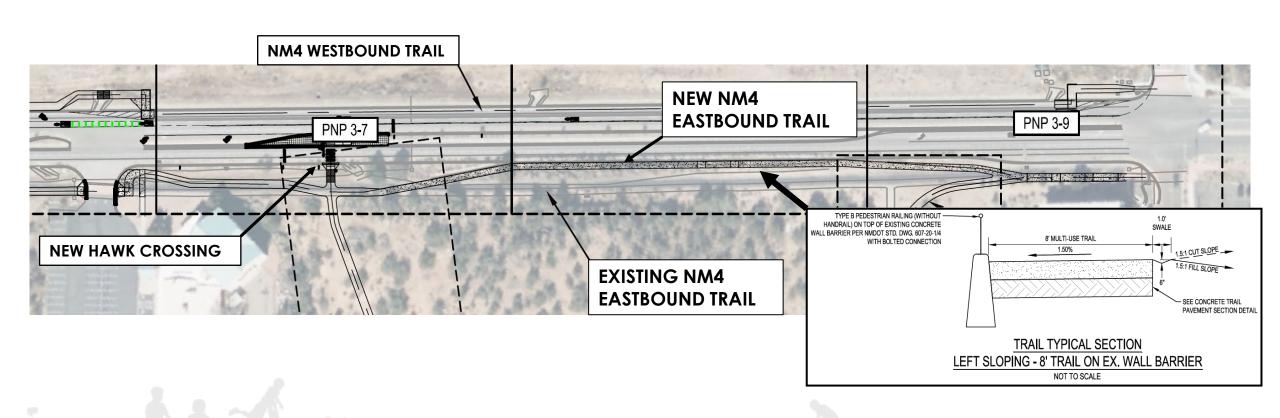






PROJECT DETAILS PINON PARK

- ~3000 linear feet of existing trail reconstruction
- ~750 linear feet of new trail
- Sidewalk connection to Sherwood Blvd
- Sidewalk connection to Sierra Vista Dr
- Replacing the existing timber bridge
- Drainage improvements

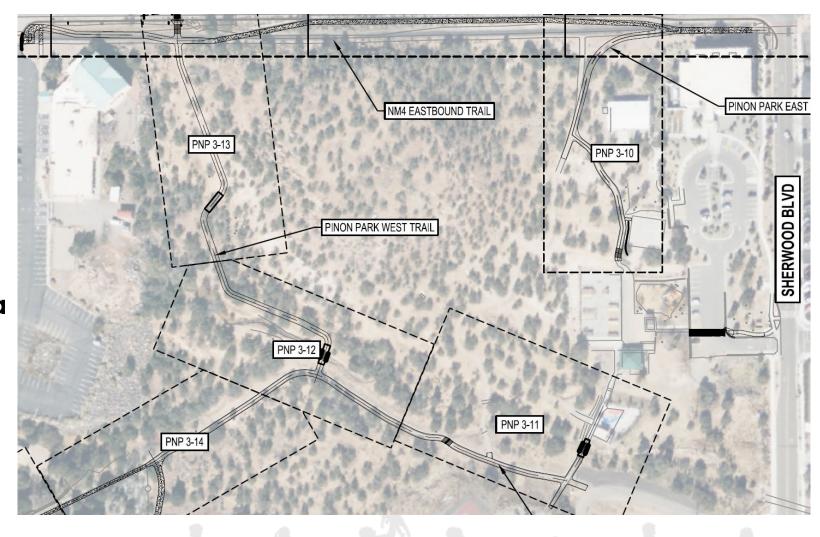









PINON PARK


Existing Conditions







PROJECT SCHEDULE

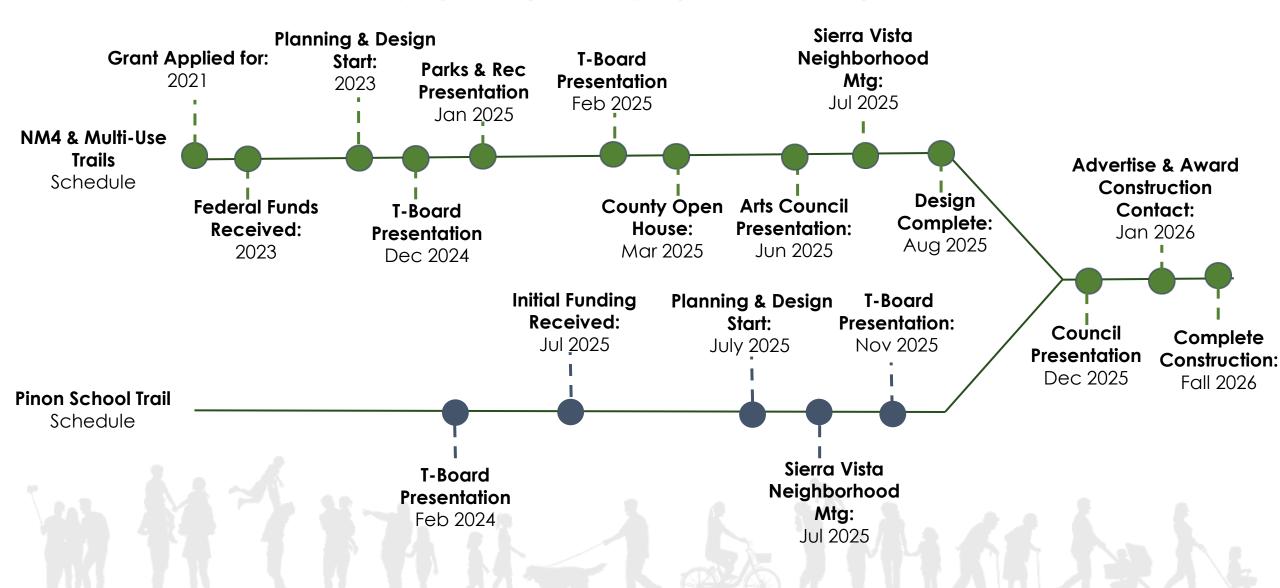









QUESTIONS?









Thank You!

The Public Works Department staff thanks you for taking time out of your busy schedule to participate in the design and construction of this important public project!





